
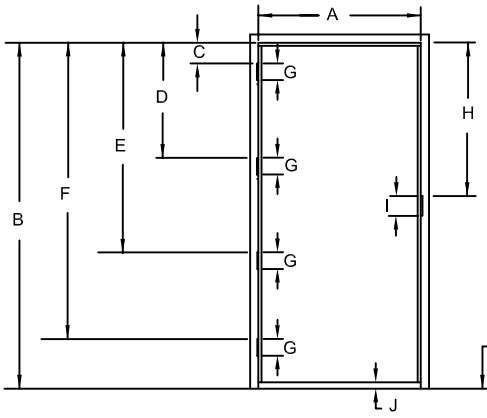




LANMOR SERVICES INC.

**SINGLE OPENING**

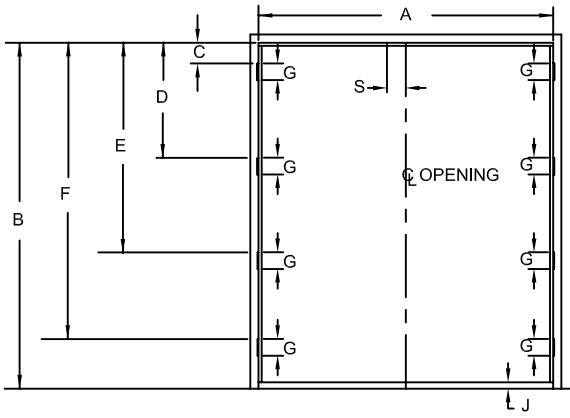



LANMOR SERVICES INC.


**PAIR OPENING**

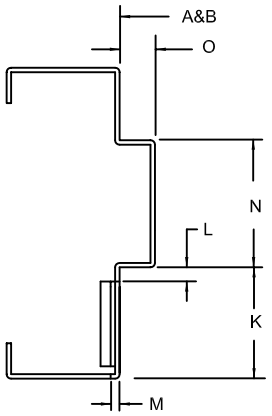


FRAME PROFILE

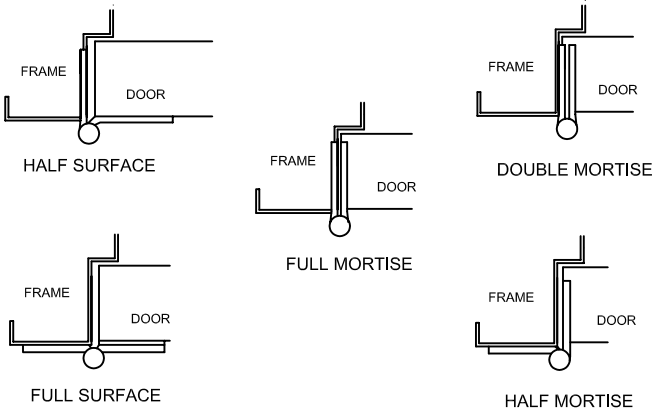


HINGE MOUNTING
CIRCLE THE APPROPRIATE HINGE CONFIGURATION

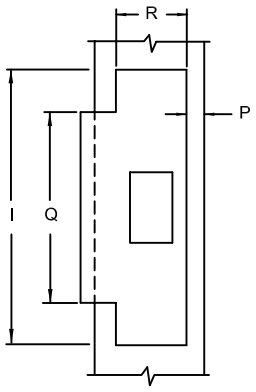


STRIKE DETAIL


| | DESCRIPTION OF DIMENSION | ACTIVE DOOR | INACTIVE DOOR | NOTES |
|---|---|---|---|---|
| A | JAMB OPENING WIDTH (RABBET TO RABBET) | | | |
| B | JAMB OPENING HEIGHT (HEAD RABBET TO FINISH FLOOR) | | | |
| C | HEAD RABBET TO TOP OF TOP HINGE | | | |
| D | HEAD RABBET TO TOP OF SECOND HINGE | | | |
| E | HEAD RABBET TO TOP OF THIRD HINGE | | | |
| F | HEAD RABBET TO TOP OF FOURTH HINGE | | | |
| G | HEIGHT OF HINGE CUTOUT | | | |
| H | HEAD RABBET TO TOP OF STRIKE | | | |
| I | HEIGHT OF STRIKE CUTOUT (NOT THE STRIKE LIP) | | | |
| J | THRESHOLD HEIGHT | | | |
| | | | | |
| K | RABBET DEPTH | | | |
| L | HINGE BACKSET | | | |
| M | HINGE DEPTH | | | |
| N | STOP WIDTH | | | |
| O | STOP HEIGHT | | | |
| | | | | |
| P | STRIKE BACKSET | | | |
| Q | LENGTH OF STRIKE LIP | | | |
| R | STRIKE WIDTH | | | |
| | | | | |
| S | ℄ OPENING TO ℄ OF FLUSHBOLT CUTOUT | | | |

**ANCHOR**

- ☐ Compression Anchor
- ☐ Existing Opening
- ☐ Metal Stud
- ☐ Masonry “T”
- ☐ Wood Stud
- ☐ No Anchors

**CONSTRUCTION**

- ☐ Knock Down
- ☐ Welded





**FIRE LABEL**

- ☐ 3 Hour
- ☐ 90 Minute
- ☐ 45 Minute


**3 Pc. Knockdown Frames** ☐ Gauge

Throat Size




**Welded Frames** ☐ Gauge

Throat Size




LANMOR SERVICES INC.




PROJECT NAME:

SALES ORDER NO:

SALESMAN:
